


REFERENCE DETAIL:

HI-PERF RIDGE VENT

SLOPE TO SLOPE, SHINGLED, FIELD ROOFED VERSION

Z BRACKET, INTERMITTENT SPACERS AND EXPANDED METAL SUPPORT SCREEN ARE ALL FACTORY ASSEMBLED

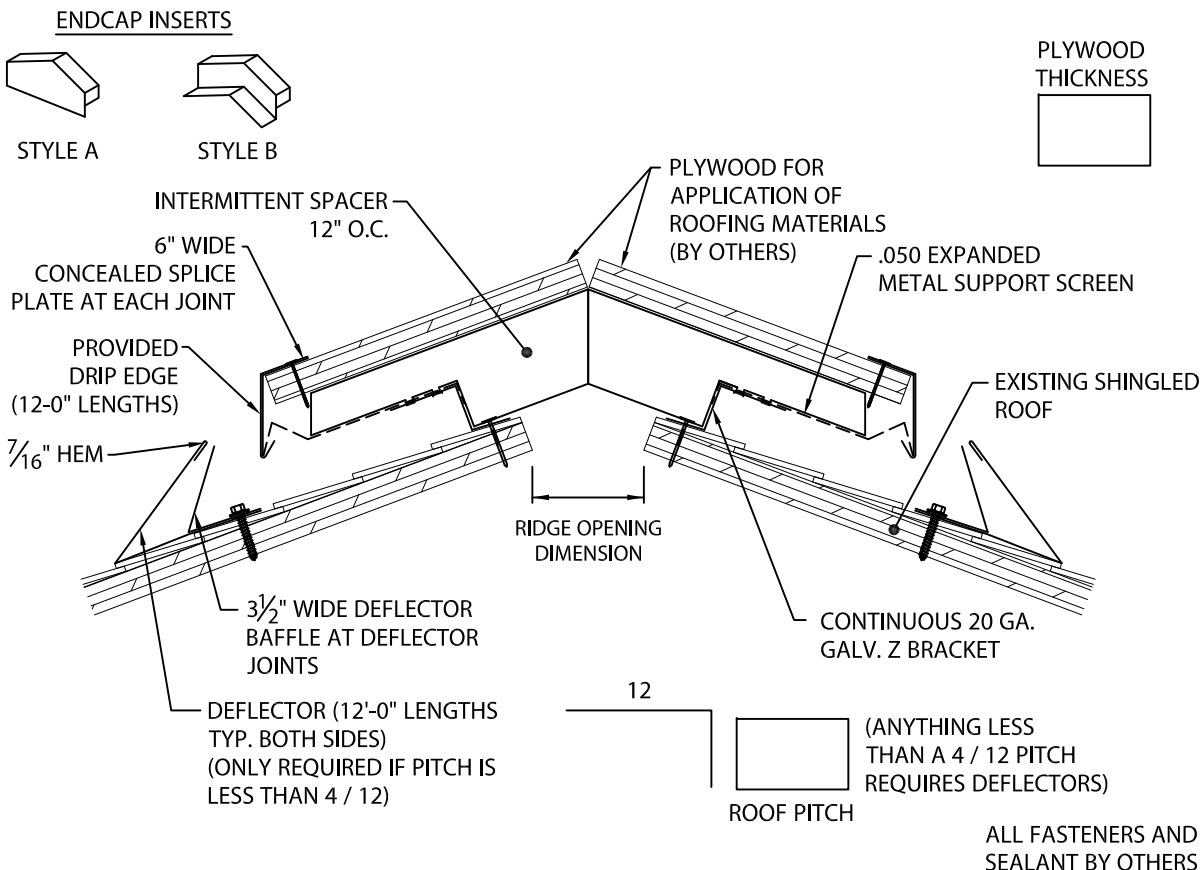

THE RIDGE OPENING MAY BE PROVIDED BY ONE OF TWO METHODS:

1. THE ACTUAL KNOWN

RIDGE OPENING OR NFA

OR

2. FIELD OR PLAN CONDITION MEASUREMENTS:

ACTUAL LINEAL FOOTAGE OF RIDGE ACTUAL LINEAL FOOTAGE OF EAVE

VENTILATION TYPE:

VENTED NAILBASE

_____ AIR SPACE DIMENSION OF VENTED NAILBASE

OR

ATTIC

_____ ATTIC FLOOR SQUARE FOOTAGE

_____ RIDGE BEAM WIDTH IF APPLICABLE

ALL FASTENERS AND SEALANT BY OTHERS

Fabrication will proceed only after receipt of signed print approval.

Print Approval:

Architect and/or contractor shall verify all dimensions, sizes and quantities. All products to be installed in strict accordance with Metal-Era's printed instructions.

Approved by: _____

Date: _____

COVER MATERIAL:

- 24 GA. GALV. STEEL
- .040" ALUMINUM
- .050" ALUMINUM
- .063" ALUMINUM
- OTHER _____

COLOR: _____ FINISH: _____

QUANTITIES:

_____ LINEAL FEET (12'-0" LENGTHS)

_____ ENDCAP INSERT(S) (COVER ONLY)

_____ STYLE A _____ STYLE B

PROJECT:

ARCHITECT:

CONTRACTOR:

REPRESENTATIVE:



Phone: 800-558-2162
Fax: 800-770-3934
www.metalera.com

DATE: 08/01/17

SHT.# ___ OF ___

DRN BY: JAB

CKD BY: SAK

DWG# 31024-20146

E
