NOTE: Indicate slope by circling appropriate outside face.

RIGHT TRANSITION

OUTSIDE FACE

SPECIFY WALL SIZE

SPECIFY WALL SIZE

OUTSIDE FACE

☐ Standard Leg Lengths
☐ Custom Leg Lengths _____

LEFT TRANSITION

OUTSIDE FACE

OUTSIDE FACE

SPECIFY WALL SIZE
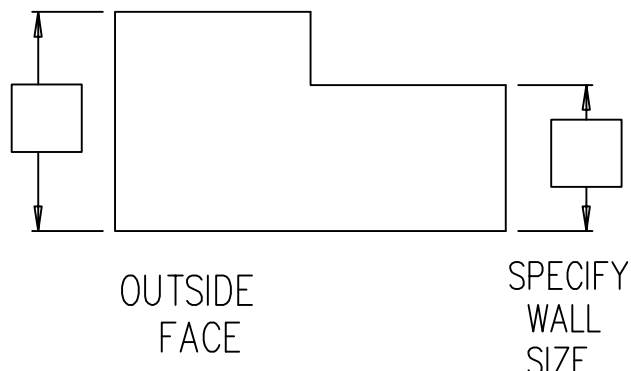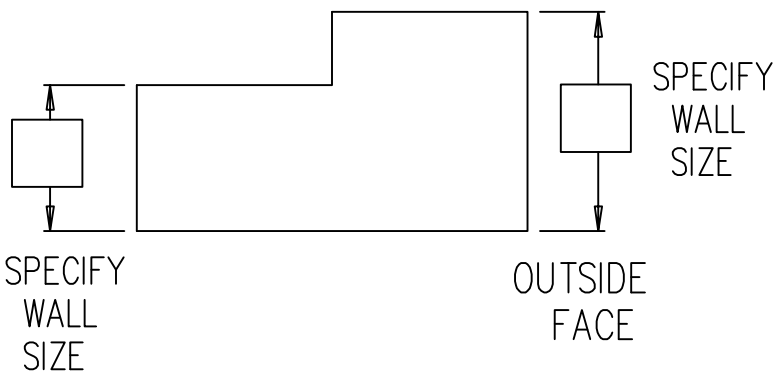
☐ Standard Leg Lengths
☐ Custom Leg Lengths _____

NOTES:
-- Concealed splice plates are provided with factory applied dual non-curing sealant strips.

-- Unless otherwise noted, fabrication of miters and accessories are furnished standard utilizing a non-penetrating Quicklock Joint, then factory sealed watertight.

Fabrication will proceed only after receipt of signed print approval.

Print Approval:

Architect and/or contractor shall verify all dimensions, sizes, and quantities. All products to be installed in strict accordance with Sika Sarnafil printed instructions.

Approved by: _____

Date: _____

-- Welded Miters and Accessories
Check one   ☐ Required (surcharge)   ☐ Not applicable

MATERIALS:
___ 24 GA. (.65 mm) Steel
___ .040" (1.01 mm) Aluminum
___ .050" (1.27 mm) Aluminum
___ .063" (1.60 mm) Aluminum
___ Other _____
Color: _____
Finish: _____
___ Smooth   ___ Textured (Stucco)

QUANTITIES:

___ Right

___ Left

☐ TAPERED   ☐ FLAT

PROJECT	Sika Sarnafil Inc.
ARCHITECT	100 Dan Road
ROOFING CONTRACTOR	Canton, MA 02021
REPRESENTATIVE/DISTRIBUTOR	(800) 451-2504
	Fax: (781) 828-5365

DATE: 06/01/02	SHT.#_____ OF _____	
DRN BY: COB		
CKD BY: SAK	DWG# 14011-2860	B

Sika® Sarnafil®
